IT'S POSSIBLE.



Dear Colleagues,

Mount Elizabeth™

RELOCATING & DECANTING



SOFT LAUNCH OF MEH'S CORPORATE OFFICE @TONG BUILDING LEVEL 7

Earlier this month,

Mount Elizabeth Hospital's Corporate Office had shifted to Tong Building Level 7. Conducted over three phases, this move will see us free up more non-clinical space within the Hospital, and also gives our staff a fresh new environment to work in:

TONG BUILDING

🖨 LEVEL 7

Phase 1 With the completion, over 200 of MEH staff currently working within the hospital premise have begun their re-location since 03 Feb 2023. Some of the functions that have shifted over include:

- Bed Management Unit
- OT and Endoscopy Booking Units

Phase 2

LEVEL 9

Our Administrative Office for MediRad and Parkway Cancer Centre (PCC) will be spruced up. Projected completion date: 15 April 2023

LEVEL 6

Phase 3 Our existing space will undergo a revamp to serve our staff from various administrative functions better.

Projected completion date: 19 June 2023

For this edition of Renaissance, I will provide updates on the following:

(1) Immediate Hoarding Plans & Future Uses

(2) Temporary Re-location of Non-Invasive Cardiac Lab (NICL) PROJECT RENAISSANCE NEWSLETTER

Issue 04 March 2023

TABLE OF CONTENTS

Introduction• P.1

Hoarding Plans & Uses• P.2-3

NICL• P.4

Phasing Plan• P.5



BED MANAGEMENT & OT UNITS

The Bed Management & OT Booking Units have commenced their operations at Tong Building and we will progressively move the Endoscopy Booking Unit over.



SOFT LAUNCH OF BMU OFFICE @TONG BUILDING LEVEL 7



Immediate Hoarding Plans & Future Uses

Construction & Demarcated Lines

Many of you have approached me to find out what the demarcated areas (outlined by masking tape) within the Hospital compound will be converted into. In the near future, construction hoardings will be/ have been put up along these demarcated lines:





- 1. Former UOB site (Level 1) Hoarded up since 4 Feb 2023 Future site of our:
 - Laboratory (Phlebotomy and Specimen Collection Clinic)
 - Executive Health Screeners

H

2.

5.

- Former Guardian site (Level 2) Hoarded up since 3 Jan 2023
 - Part of the future site of our Laboratory
- Former Fruit Shop; SingaFresh site (Level 2) Hoarded up since 20 Feb 2023
 Future site of an F&B outlet
 - Former Delifrance site (Level 2) Reinstated
 - Part of a new public corridor/ circulation area in future.
 - Level 2 Carpark Hoarded up since 16 Jan 2023
 - This site, along with current Hospital Testing Centre (HTC) and Swab Centre, will be reinstated as a carpark in end 2025.



CLOSURE OF TOWER B LIFTS



Closure of three Block B Lifts J, K and L from Levels 1 through 10, progressively from Friday, 3 Mar 2023

- This is to improve accessibility, operational efficiencies and interdependencies.
- Larger lift core comprising passenger and service lifts facing the public and back-of-house service corridors respectively in the future with updated fire protection compliance.

LIFT MITIGATION PLANS

Remaining Lifts at Block B:

- Lift M Serves L1 L2, L6 L10
- Lift N Serves L1 L10

Priority for Lift Usage:

- Medical Emergencies (Security will override)
- Patient transfers


To minimise the queues at Lift Lobby B, we encourage our staff & doctors to take the stairs or use Lift Lobby C for L1 - L5 whenever possible.



PHASE 4a BLOCK B Level 1(Lift) 03 Mar 2023 to 16 Nov 2023



PHASE 4a BLOCK B Level 2 (Lift) Site Possession: 03 Mar 2023 to 16 Nov 2023





7.

- Carpark lots outside carpark exit gantry Level 1 Hoarded up since 23 Feb 2023
 - Alimak (Construction lift) will be built on this site and used for logistics of construction materials.







Block C Roof top, outside Ward 4B - Hoarded up since 23 Feb 2023This site is used as worker rest area.











OUR FIRST WARD TO RELOCATE

Ward 4B

Hoarded up since 17 Feb 2023 Future site usage:

 New Endoscopy procedure rooms which include a brand New Endoscopic retrograde cholangiopancreatography (ERCP) suite, as part of our right-siting objective.

Please be assured that at each of these hoarded areas, proper precautions will be/ have been taken to ensure the safety of our patients, public, our doctors and staff.

TEMPORARY RE-LOCATION OF NON-INVASIVE CARDIAC LAB (NICL)


As our major works along the corridors of Level 2 between Medical Centre & Hospital will be commencing soon, our NICL will be temporarily re-located to the Nursing Administration Office and Victoria Lounge, both located at MEH Level 5, the relocation will commence from May 2023.

Our future NICL will be part of the new major 16,778 square feet Radiology on Level 2 (where our current Laboratory, Business Office, Radiology, Medical Record Office, Casemix, IT and Despatch offices are located). The targeted completion date is Q4 2024.

Jorg yih Mine

Mr Yong Yih Ming Chief Executive Officer Mount Elizabeth Hospital

RENAISSANCE RENOVATION PHASE

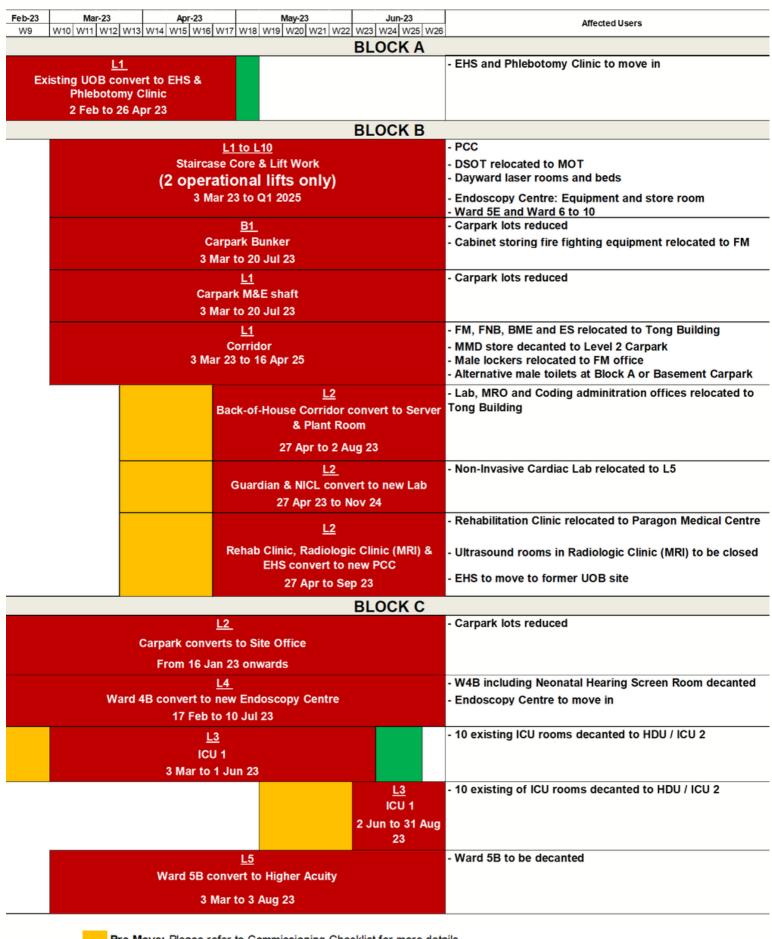

Pre Move: Please refer to Commissioning Checklist for more details

Construction: Preparation for equipment and consumables procurement and installation, licensing and staff training **Takeover:** Equipment testing and commissioning, staff orientation etc. Go Live.

*Pending further discussion

M&E - Mechanical and Enginneering
